

Phase 1 Implementation Framework


A 13-week engagement that takes a custom home builder or remodeler from signed contract to a trained Success Champion running a fully-adopted JobTread system.

CURRENT TRACK

Moderate

4-week build · 7-week rollout · 1-week handoff

Build Complexity Scorecard: 89-139



Build-out phase work Team rollout phase Champion call Milestone invoice

PHASE	DISCOVERY	BUILD-OUT PHASE	BUILD-OUT PHASE	BUILD-OUT PHASE	BUILD-OUT PHASE	ROLLOUT PHASE	ROLLOUT PHASE	ROLLOUT PHASE	ROLLOUT PHASE	ROLLOUT PHASE	ROLLOUT PHASE	ROLLOUT PHASE	HANDOFF
	W0 KICKOFF	W1	W2	W3	W4	W5	W6	W7	W8	W9	W10	W11	W12 HANDOFF
WEEKLY CALL <i>1 hour, with team</i>	Discovery + scope confirmation, Champion identified, kickoff	Cost catalog construction, customer pipeline build-out, u...	Budget templates with formulas, plans tab, parameter library	Schedule templates, selections catalog, allowances, packages	Customers/jobs loaded, integrations verified, Champion ready	Messaging, to-dos, daily logs go live (Tier 1 habits)	Budgets go live (the heartbeat)	Plans and schedules	Time tracking	Selections and allowances	Documents, files, proposals, contracts	Change orders, POs, invoicing, cost tracking	Dashboards, KPIs, Support Lab onboarding
CHAMPION CALL <i>30 min, weekly</i>	SC: Stepping into the Role	SC: Owning Your Own Learning	SC: Holding the Team to New Habits	SC: Reading the Room	SC: Becoming the Question Person	SC: Working with the Heartbeat	SC: Connecting the Dots	SC: Closing the Loop	SC: Carrying the Customer Experience	SC: Standing Behind the Process	SC: Standing Behind the Process	SC: Closing the Books with Confidence	SC: Carrying It Forward
INVOICES <i>Milestone billing</i>		INVOICE #1				INVOICE #2				INVOICE #3			

REPEATABLE PATTERN

The Rollout Playbook

Every team rollout, regardless of which week or which tool, follows the same four-step pattern. The team learns the rhythm, which makes change predictable.

STEP 1

Pre-Approval

One week before. Slide deck and Loom sent to leadership and Champion. Approval required on readiness and accuracy before kickoff.

STEP 2

Team Kickoff

Day 1 of rollout week. Live Zoom with full team. Champion co-leads. Recorded for absent and reference.

STEP 3

Practice Week

Days 2 to 5. Team uses the tool in real work. Champion is first point of contact. Consultant monitors adoption remotely.

STEP 4

Adoption Check

End of rollout week. Champion and consultant review who is using it, who is not, what is breaking. Refine before next week.

DELIVERABLE TOOLKIT

The Seven Tools

Each tool is built for a specific moment in the engagement. The workflow flows top to bottom from Phase 0 through Phase 1 close.

1

Build Complexity Scorecard

Phase 0 · After audit, before Discovery & Review call

Score the audit, get track recommendation, document the assignment.

↓

2

Discovery & Review Report

Phase 0 · Delivered at Discovery & Review call

Six-tab interactive HTML covering findings, gap analysis, workflow map, team assessment, platform audit, and Phase 1 scope.

↓

3

Scope Confirmation Templates

Week 0 · Before kickoff meeting

Track-specific markdown templates pasted into JobTread custom document, signed by client.

WEEKLY 30-MIN CALL

Champion Session Structure

Every Champion call follows the same seven-element structure. Back-to-back with the 1-hour team call, same day.

1

Accountability Check

What they committed to last week and how it went

2

Review the Playbook Chapter

What landed, what did not, questions surfaced

3

Reflection Questions

Listen to what is happening on the team

4

Talking Points

Leadership coaching content for the week

5


Watch-Fors

Specific behaviors to notice in the team

6

Self-Sufficiency Drill

Scenario or question they work through alone

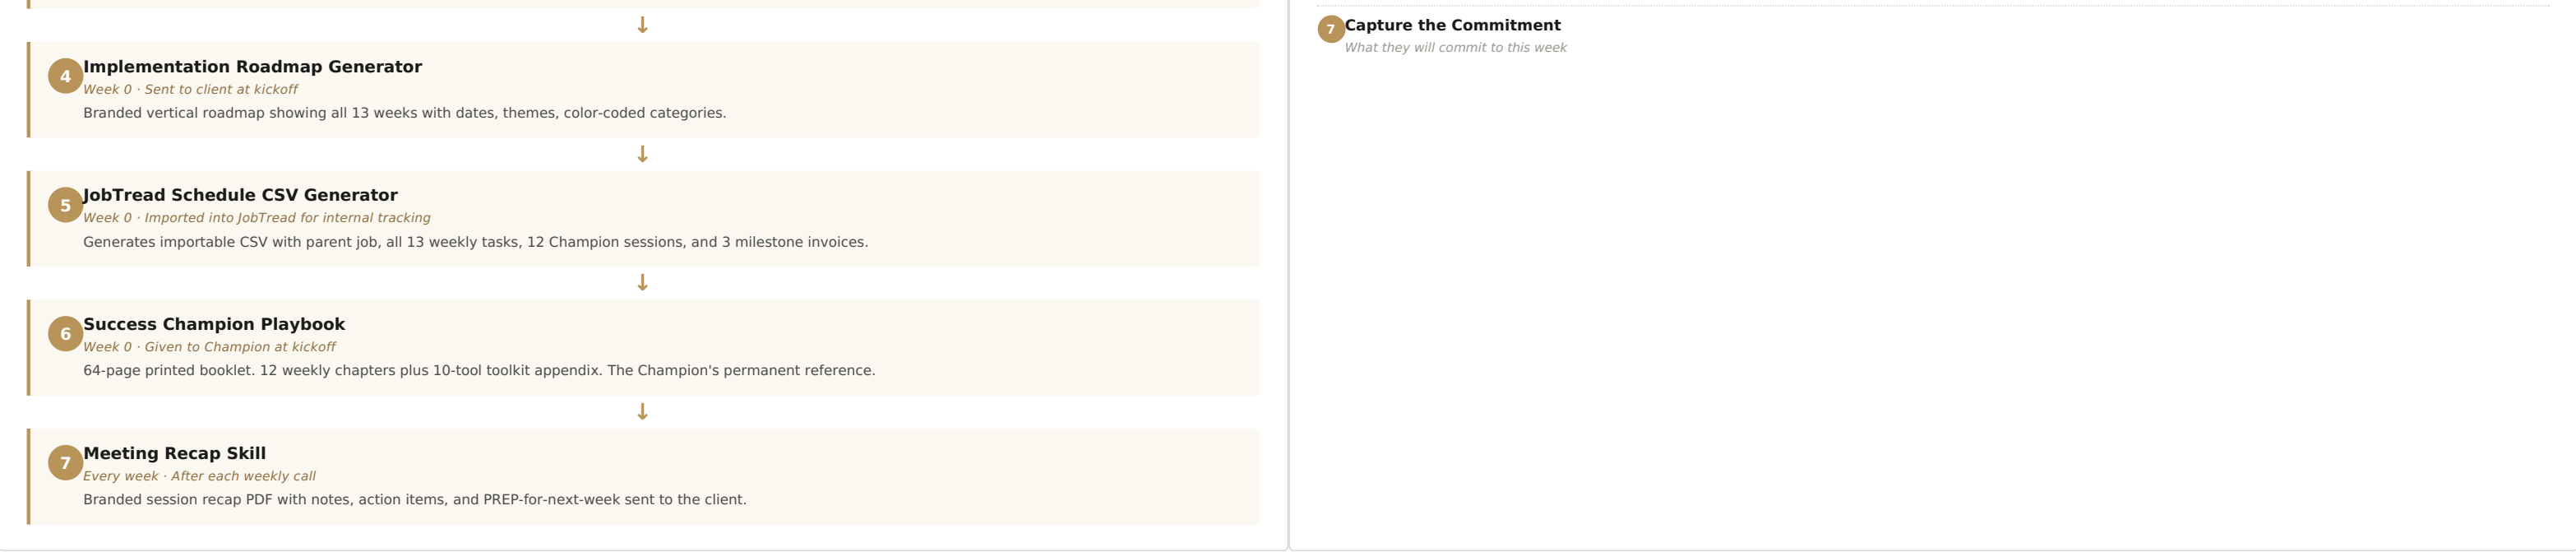

PRINCIPLE 01 Lowest Friction First Team rollout starts with tools that have no dependencies and the lowest cognitive load. Habit-building first. Heavy tools layer on once the daily JobTread habit is real. Sequence is dependency-driven, not friction-driven.	PRINCIPLE 02 Champion-Led, Not Consultant-Led The consultant is temporary. The Champion is permanent. Every team rollout is co-led by the Champion. By Week 12, the Champion runs the system. We have built a leader, not just configured a tool.	PRINCIPLE 03 Repeatable Playbook, Every Time Every team rollout follows the same 4-step pattern. Every Champion call follows the same 7 elements. Every engagement starts with the same scorecard. Repetition is the point. Predictability is what makes adoption stick.
--	---	--

Let's build something that lasts.
